




National Taxpayers Association  
pesa zetu, haki yetu

# CITIZEN'S CDF REPORT CARD

Mumias Constituency, Mumias District



# Citizen's Constituency Development Fund Report Card for Mumias Constituency, Mumias District



National Taxpayers Association  
**pesa zetu, haki yetu**

© National Taxpayers Association  
March, 2010

This publication was made possible through support provided by the Department for International Development (DfID), Canadian International Development Agency (CIDA), Swedish International Development Cooperation Agency (SIDA) and German Technical Cooperation (GTZ).

The findings expressed herein are those of the NTA and they do not necessarily reflect the views of our partners.

## TABLE OF CONTENTS

<b>1.0</b>	<b>Introduction</b>	<b>1</b>
<b>2.0</b>	<b>Executive Summary</b>	<b>1</b>
	<b>Table 1: CDF Allocations to Mumias Constituency (FY) 2003/04 - 2007/08</b>	<b>1</b>
<b>3.1</b>	<b>Recommendations for Hon. Benjamin Washiali</b>	<b>2</b>
<b>3.2</b>	<b>Recommendations for the CDF Board</b>	<b>2</b>
	<b>Table 2: Summary of Findings from NTA Audit of CDF Projects (FY)2006-07</b>	<b>3</b>
	<b>Table 3: Summary of Findings from NTA Audit of CDF Projects (FY)2007-08</b>	<b>4</b>
<b>4.0</b>	<b>NTA Research Methodology</b>	<b>5</b>
	<b>Annex 1: Project Classification Summary Tables, Project Profiles and digital photographs for all CDF projects visited and assessed in the Financial Year (FY) 2006-07</b>	
	• Category A projects	8 - 17
	• Category B projects	18 - 21
	• Category C projects	22 - 45
	• Category E projects	46 - 52
	<b>Annex 2: Project Classification Summary Tables, Project Profiles and digital photographs for all CDF projects visited and assessed in the Financial Year (FY) 2007-08</b>	
	• Category A projects	54 - 71
	• Category B projects	72 - 79
	• Category C projects	80 - 97
	<b>Annex 3: CDF Project Rapid Assessment Form</b>	<b>98</b>
	<b>Annex 4: CDF Project Users' Questionnaire</b>	<b>99</b>
	<b>Annex 5: Technical Project Assessment Form</b>	<b>101</b>
	<b>Annex 6, 7 &amp; 8: Correspondence between NTA and area Member of Parliament</b>	<b>102 - 105</b>

## 1.0 Introduction

- This Citizen's Report Card has been researched and published by the National Taxpayers Association (NTA) to sensitize citizens, elected representatives, government officials and civil society organizations on the management of the Constituency Development Fund (CDF).
- The NTA is a national, independent, non-partisan organization focused on improving the delivery of services and the management of devolved funds for the benefit of all Kenyans.
- The NTA is supervised by a Governing Council of prominent civil society and private sector leaders. The day to day operations of the NTA are managed by the NTA Secretariat based in Nairobi and eight Regional NTA offices located in the provincial headquarters. The NTA is establishing Constituency Monitoring Committees of volunteers at the constituency level across Kenya.
- The NTA has researched and published Citizen's Report Cards in 49 constituencies from all provinces in Kenya. The NTA will cover all 210 constituencies by December 2010.
- This Citizen's Report Card presents findings from research in Mumias Constituency, Mumias district. The report covers two government Financial Years -- 2006/07 and 2007/08. The NTA has not researched the 2008/09 Financial Year as funds have not been allocated and/or spent to date.
- The monitoring exercise was conducted between January and May 2009.
- It is important to note that the two Financial Years (06/07 & 07/08) were simply used to set the scope of the work based on NTA's interest but financial reporting takes into consideration accumulated allocations to the monitored projects over the years.

## 2.0 Executive Summary

- A summary of total funds allocated to Mumias Constituency is listed in Table 1 below. A total of **Kshs. 181,275,626** has been allocated to the constituency since 2003/04.
- The main findings from NTAs research in Mumias Constituency are listed in Table 2 and Table 3 below.
- Project profiles and digital photographs of all CDF projects visited and assessed are listed in Annex 1 and Annex 2.
- Correspondence and minutes of NTA meetings with the area Member of Parliament on the Constituency Citizen Report Card are listed in Annex 6, Annex 7 and Annex 8.

**Table 1: CDF Allocations to Mumias Constituency 2003/04 - 2007/08**

Constituency Name	2003/2004	2004/2005	2005/2006	2006/2007	2007/2008	Total
Mumias	6,000,000	29,769,752	38,501,883	53,337,276	53,666,715	<b>181,275,626</b>

- The key findings for projects funded and monitored in Financial Year 2006/2007 are as follows:  
**Kshs. 5,950,000 of taxpayers' money has been wasted due to badly implemented projects**  
7% of the total CDF funds allocated to the monitored projects in FY 2006-07 were on ineffective projects  
**Kshs. 4,700,000 of taxpayers' money has been wasted due to abandoned projects**  
5% of the total CDF funds allocated to the monitored projects in FY 2006-07 were on abandoned projects

- The key findings for projects funded and monitored in Financial Year 2007/2008 are as follows:  
**Kshs. 14,470,000 of taxpayers' money has been wasted due to badly implemented projects**  
16% of the total CDF funds allocated to the monitored projects in FY 2007-08 were on ineffective projects  
**Kshs. 2,030,000 of taxpayers' money is unaccounted for**  
2% of the total CDF funds allocated to the monitored projects in FY 2007-08 are unaccounted for

### **3.1 Recommendations for Hon. Benjamin Washiali**

1. Complete all incomplete CDF projects by the end of FY 08 - 09.
2. Trace and fully account for all missing funds.
3. Reduce by 80% badly implemented CDF projects in FY 08-09.
4. Make available all records of CDF projects, plus Bills of Quantities

### **3.2 Recommendations for the CDF Board**

1. Ensure quick response to requests for reallocation of funds from the Constituency Development Fund Committees (CDFCs). The Board is widely accused of delay in approving decisions on reallocation of funds at the constituency level.
2. Regularly update the information listed in the Project Status Reports on the CDF web site to ensure that accurate and up to date information is available to the public.

**Table 2: Summary of Findings from NTA Audit of CDF Projects (FY) 2006-07 in Mumias Constituency**

Category	Project Assessment Classification	No. of Projects	Budget Awarded	Budget Spent	Budget Unaccounted For
			Kshs.	Kshs.	Kshs.
A	<b>Well built, completed projects</b> - good quality construction, good value for money for taxpayers'.	19	20,748,515	20,748,515	-
B	<b>Badly built, complete and incomplete projects</b> - poor quality construction, money wasted, poor value for money	8	5,950,000	5,950,000	-
C	<b>Well built, incomplete projects</b> - project not yet complete, being built in phases, so far well built	48	56,762,705	56,762,705	-
D	<b>Abandoned Projects</b> - projects are incomplete and not funded in the last year, taxpayers' money is wasted	14	4,700,000	4,700,000	-
E	<b>Ghost projects</b> - officially allocated funds, but project does not physically exist	-			-
<b>TOTAL</b>		<b>90</b>	<b>88,161,220</b>	<b>88,161,220</b>	<b>-</b>

Main Findings	Summary of Funds (Kshs.)	% of Total
<b>Total Money Badly Used (B Projects)</b>	5,950,000	7%
<b>Total Money Wasted (D Projects)</b>	4,700,000	5%
<b>Budget Unaccounted For</b>	-	-

**Table 3: Summary of Findings from NTA Audit of CDF Projects (FY) 2007-08 in Mumias Constituency**

Category	Project Assessment Classification	No. of Projects	Budget Awarded	Budget Spent	Budget Unaccounted For
			Kshs.	Kshs.	Kshs.
<b>A</b>	<b>Well built, completed projects</b> - good quality construction, good value for money for taxpayers'.	<b>35</b>	33,255,284	33,255,284	0
<b>B</b>	<b>Badly built, complete and incomplete projects</b> - poor quality construction, money wasted, poor value for money	<b>15</b>	14,470,000	14,470,000	0
<b>C</b>	<b>Well built, incomplete projects</b> - project not yet complete, being built in phases, so far well built	<b>35</b>	40,872,436	40,872,436	0
<b>D</b>	<b>Abandoned Projects</b> - projects are incomplete and not funded in the last year, taxpayers' money is wasted	<b>0</b>	0	0	0
<b>E</b>	<b>Ghost projects</b> - officially allocated funds, but project does not physically exist	<b>17</b>	2,030,000	0	2,030,000
<b>TOTAL</b>		<b>102</b>	<b>90,627,720</b>	<b>88,597,720</b>	<b>2,030,000</b>

Main Findings	Summary of Funds (Kshs.)	% of Total
<b>Total Money Badly Used (B Projects)</b>	14,470,000	<b>16%</b>
<b>Total Money Wasted (D Projects)</b>	0	<b>0</b>
<b>Budget Unaccounted For</b>	2,030,000	<b>2%</b>

## 4.0 NTA Research Methodology

The research methodology involved the following stages and methods.

### 1. Secondary Data Collection and Analysis

NTA Research Officers held a series of meetings with district and constituency officials to collect information on CDF projects funded in FY 2006/07 and 2007/08.

### 2. Project Site Visit, Rapid Assessment, and User Interviews

NTA Research Officers visited all selected CDF projects funded in FY 2006/07 and 2007/08. At each project site they:

- i. took digital photographs of the project;
- ii. undertook a rapid assessment of the project using a structured Project Rapid Assessment Form (see Annex 3)<sup>1</sup>.

### 3. Desk-based Project Classification

Upon returning from the field NTA Research Officers analysed the data collected and then classified all projects into one of the following five categories:

#### Category A Projects – Well implemented, completed projects

- This category was for CDF projects which had scored above 15 marks out of 30 on the Project Rapid Assessment Form (Annex 3)<sup>2</sup>, and were found to be well built, with good value for money (i.e. the budget was the right amount for the infrastructure delivered).

#### Category B Projects – Badly implemented, complete and incomplete projects

- This category was for CDF projects which had scored less than 15 marks out of 30 on the Project Rapid Assessment Form, and were found to be poorly constructed with poor value for money, and/or with budgets much larger than what was actually delivered.

#### Category C Projects – Well implemented, incomplete projects

- This category was for CDF projects which had scored above 15 marks out of 30 on the Project Rapid Assessment Form, and were projects well implemented but incomplete, i.e. money had been used to build a structure of good quality, but the construction is incomplete.

#### Category D Projects - Abandoned Projects

- This category of projects are incomplete and did not receive financial allocation in the subsequent Financial Year. It should be noted that the CDF Act provides for continuous allocation to projects until completion.

#### Category E Projects – Ghost projects

- This category was for CDF projects which had been officially allocated funds but the project did not physically exist at the time of study i.e. it was a ghost project.

---

<sup>1</sup>The data listed in this form was based on the findings from interviews with project users

<sup>2</sup>The Research Officer gave each project a score out of 30 marks for: (1) Community participation in project selection/community users satisfaction with the project (10 marks); (2) Project completion status - on time/within budget? (10 marks); and, (3) Visual assessment of overall quality of construction and finish (10 marks).

### **Category F Projects – Reallocated Funds**

- This category was for CDF projects that were not implemented for the reason that the funds were reallocated to other projects and with authority from the CDF Board in accordance with the CDF Act.

### **4. Desk-based Independent Technical Assessment and Strategic Visits**

At this stage NTA Research Officers contracted a local engineer (or quantity surveyor) to undertake an independent desk review which involved: (i) analysis of secondary data and data collected in the field; (ii) strategic field visits to selected projects where additional information was needed; and, (iii) classification of all projects into one of the six categories above.

### **5. Desk-based Analysis and Final Project Classification**

Following the independent technical assessment, the NTA Research Officer met with the contracted engineer or quantity surveyor to compare her/his list of categorised projects. The output of this meeting was a final list of categorised projects.


### **6. Comments and Review**



Following the elaborate process of compiling the Citizen's Report Card, the NTA developed a draft report of the findings. This report was then sent to the area Member of Parliament (copied to the CDF Board) for his/her comments (see letter in Annex 6). The MP was given a period of one month to comment on the draft report. In cases where the NTA did not receive any communication a reminder letter was sent (see Annex 7) at the end of week four. If the NTA had no comments by the end of week six then the draft CDF CRC was processed for publishing.



In response to comments from the NTA, a number of MPs requested a meeting to discuss our findings or sent letters with comments (See the list of MPs who requested for the meeting or sent their comments in Annex 8). The NTA considered all comments and made changes in the draft CDF CRC where we had adequate supporting documentation.



## Annex 1


Project Classification Summary Tables,  
Project Profiles and digital photographs  
for all CDF projects visited and assessed in  
the Financial Year (FY) 2006 - 07


<b>Project Number</b>	CDF/027	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebwaliro primary	
<b>Project Activity</b>	Construction of 2 classes	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete and in Use	
<b>Total Funds Awarded to Date</b>	950,000	
<b>Total Funds Spent to Date</b>	950,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	90%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is of good quality and decently finished as manifested by the aesthetic steel glass, glazed window and doors, and beautifully landscaped site.	



<b>Project Number</b>	CDF/029	 
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eluche Secondary	
<b>Project Activity</b>	Construction of administration block	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,500,000	
<b>Total Funds Spent to Date</b>	1,500,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	87%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	Good quality materials and construction work, well painted. Good value for money for the community.	



<b>Project Number</b>	CDF/031	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emachina primary	
<b>Project Activity</b>	Administration block and renovation of 8 classrooms	
<b>Location/Ward</b>	Nabongo/Ekero	
<b>MPs Name</b>	Hon. Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,410,000	
<b>Total Funds Spent to Date</b>	1,410,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	67%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The new structure is well implemented but renovated classrooms have not been painted. Generally though, there is value for the taxpayers' money.	



<b>Project Number</b>	CDF/073	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mukambi Baptist primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	23/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was jointly supported by CDF and LATF kitties with the latter contributing Kshs 580,000. Total CDF contribution to the project was Kshs 1,400,000. The project has been well implemented and the finishing is up to standard. There is good value for tax payers' money.	



<b>Project Number</b>	CDF/078	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mungabira primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,900,000	
<b>Total Funds Spent to Date</b>	1,900,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	Although the project cost seems to be on the upper side, the project has been well implemented and the finishing is good. It reflects value for money.	


<b>Project Number</b>	091	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Petro's primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	90%	
<b>Date of Assessment</b>	08/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is complete and well implemented. The finishing and fittings are of good quality and are a manifestation of good workmanship.	


<b>Project Number</b>	CDF104	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ahong'injo secondary school	
<b>Project Activity</b>	Construction of 3 classrooms	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	16/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project has been well implemented with a fine finish of rough cast and paint. The project reflects value for money.	



<b>Project Number</b>	CDF/114	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eluche primary	
<b>Project Activity</b>	Renovation of roof	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	100,000	
<b>Total Funds Spent to Date</b>	100,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The school received the fund from the emergency reserve kitty to restore the blown off roofs. The work was done well and the classes are presently in use. Good value for taxpayers' money.	


<b>Project Number</b>	CDF/146	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshikulu community health centre	
<b>Project Activity</b>	Constr. of a health centre	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	2,500,000	
<b>Total Funds Spent to Date</b>	2,500,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	79%	
<b>Date of Assessment</b>	10/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project that was started by a self group in the community to respond to the needs of the community members is complete and well implemented. The CDF support was a great boost to the project. The finishing's and fittings are well done and electricity is installed in the facility. It reflects good value for money.	


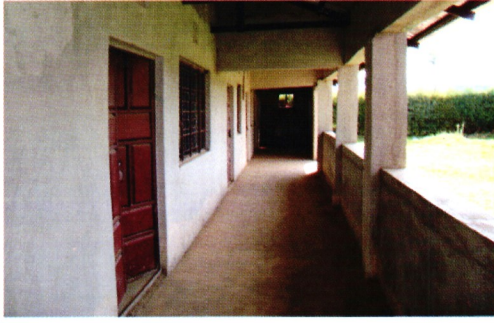
<b>Project Number</b>	CDF/156	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eluche - Mung'anga	
<b>Project Activity</b>	Construction of bridge	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	2,000,000	
<b>Total Funds Spent to Date</b>	2,000,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	76%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is well done and with guard rails fitted on the sides. Although the physical structure is well done, there is a feeling that the amount spent on the project is on the higher side. Generally though, it passes for a well implemented project, good value for money for the community.	



<b>Project Number</b>	CDF/165	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Buhuru Traders Water project	
<b>Project Activity</b>	Construction of water pump	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	150,000	
<b>Total Funds Spent to Date</b>	150,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	23/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was identified by community members and has been well implemented. The concreting around the base is strong and so is the installed steel pump. It is functional and serves the community needs. Good value for money.	

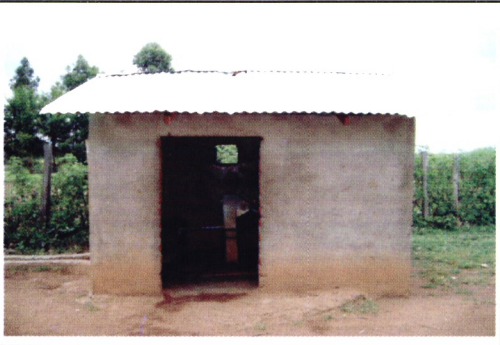

<b>Project Number</b>	CDF/181	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emuberi primary	
<b>Project Activity</b>	Water project	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	140,000	
<b>Total Funds Spent to Date</b>	140,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is well implemented with quality concrete base and steel pump. The project is serving the intended purpose and is thus a well implemented project.	



<b>Project Number</b>	CDF/196	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Indangalasia secondary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,050,000	
<b>Total Funds Spent to Date</b>	1,050,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	87%	
<b>Date of Assessment</b>	13/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project reflects good value for money. The physical structure is up to standard and the finishing is good. There is great satisfaction with the project. Good value for money.	



<b>Project Number</b>	CDF/198	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Iyabo Water Project	
<b>Project Activity</b>	Water pump maintenance	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	70,000	
<b>Total Funds Spent to Date</b>	70,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	73%	
<b>Date of Assessment</b>	18/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The pump pipes were repaired within the project cost and are working efficiently. The concrete base was however not repaired although it shows signs of depletion. Generally, the project is well implemented, hence good value for money.	


<b>Project Number</b>	CDF/213	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Munga'nga dispensary	
<b>Project Activity</b>	Construction of a health facility	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,928,515	
<b>Total Funds Spent to Date</b>	1,928,515	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The dispensary has been constructed using bricks reinforced with back column and VRC beam. Treated wood rafters have been used in roofing. Generally, the project is well implemented and reflects value for taxpayers' money.	



<b>Project Number</b>	CDF/214	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Musanda community	
<b>Project Activity</b>	Trenching and laying pipes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	440,000	
<b>Total Funds Spent to Date</b>	440,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	77%	
<b>Date of Assessment</b>	16/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	There is great community satisfaction with the project although there are feelings that trenching did not cover a wide area. Generally though, it reflects good value for money.	



<b>Project Number</b>	CDF/220	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mwitoti primary school	
<b>Project Activity</b>	Construction of water tank	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	150,000	
<b>Total Funds Spent to Date</b>	150,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project has been well implemented. Besides installation of the water pump, the money was also used to construct shelter for the facility. Good value for money for the community.	



<b>Project Number</b>	CDF/225	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Shianda community water and sanitation	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	150,000	
<b>Total Funds Spent to Date</b>	150,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	90%	
<b>Date of Assessment</b>	18/01/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The water point has been well protected and serves the school better. It is a well implemented project, hence value for money.	


<b>Project Number</b>	CDF/236	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Butende secondary school	
<b>Project Activity</b>	Construction of administration block and classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	2,210,000.	
<b>Total Funds Spent to Date</b>	2,210,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	87%	
<b>Date of Assessment</b>	04/04/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is well implemented and has been given a quality finish of painted rough cast. The fittings are good and of standard quality. It reflects value for taxpayers' money.	


<b>Project Number</b>	CDF/07	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Lureko girls sec sch	
<b>Project Activity</b>	Construction of administration block	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	1,800,000	
<b>Total Funds Spent to Date</b>	1,800,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	47%	
<b>Date of Assessment</b>	14/01/00	
<b>Project Classification</b>	B	
<b>Comments</b>	This is indeed a badly implemented project since all the amounts allocated have been spent yet it is barely 50% complete. There is no value for taxpayers' money in this project.	

<b>Project Number</b>	CDF/026	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebuyenjere primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	43%	
<b>Date of Assessment</b>	14/01/00	
<b>Project Classification</b>	B	
<b>Comments</b>	Instead of the intended construction work, the money was used in renovation of the classes. The incomplete renovation exercise has however been done using poor quality materials such as substandard timber and iron sheets for roofing. The windows are also not fitted. Although the amount in question is relatively small for the embraced activity, it should have been used to carry out quality and manageable activity.	


<b>Project Number</b>	CDF/042		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Eshihaka primary school		
<b>Project Activity</b>	Construction of 2 classes		
<b>Location/Ward</b>	South Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Complete		
<b>Total Funds Awarded to Date</b>	900,000		
<b>Total Funds Spent to Date</b>	900,000		
<b>Total Unaccounted Funds</b>	0		
<b>Technical Performance Score</b>	80%		
<b>Date of Assessment</b>	03/02/09		
<b>Project Classification</b>	B		
<b>Comments</b>	Although the project status report indicates that two new classrooms were to be constructed, the facility received a face lift – plastering and painting of the old structures at the institution. The tasks were not well done and the project seem to have used lesser money. No value for money for the community.		



<b>Project Number</b>	CDF/044 A		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	St. Andrews Eshikalame secondary school		
<b>Project Activity</b>	Borehole and pump.		
<b>Location/Ward</b>	Etenje		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Incomplete		
<b>Total Funds Awarded to Date</b>	150,000		
<b>Total Funds Spent to Date</b>	150,000		
<b>Total Unaccounted Funds</b>	0		
<b>Technical Performance Score</b>	24/02/09		
<b>Date of Assessment</b>	49%		
<b>Project Classification</b>	B		
<b>Comments</b>	The service area is of small radius and plastering and screeding work was poorly done although the pump is in use. Overall, the project is badly implemented and exhibits no value for money.		



<b>Project Number</b>	CDF/047	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ichinga primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo /Nucleolus	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	1,100,000	
<b>Total Funds Spent to Date</b>	1,100,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	47%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	B	
<b>Comments</b>	According to the project status report, 4 classrooms were to be constructed and 2 were to be renovated. The construction is incomplete and the workmanship is wanting as demonstrated by the slanting pillars supporting the verandah roofing in picture above.	



<b>Project Number</b>	CDF/116	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Elwasambi primary	
<b>Project Activity</b>	Construction of two classrooms.	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	600,000	
<b>Total Funds Spent to Date</b>	600,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	47%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The project is poorly implemented and showing signs of grave weakness even though it is incomplete. Parts of the wall already have deep cracks and threaten to crumble down. Besides, it appears the project has been left abandoned for some time as demonstrated by the growth of moulds thus exposing it to the vagaries of weather with the potential effect of increasing the cost of construction.	



<b>Project Number</b>	CDF/194	<b>Picture Unavailable</b>
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ihonje sec school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	20%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The picture tells all about this project that has so far consumed Kshs 800,000 of taxpayers' money. Sections of the building have collapsed already despite the fact that it is incomplete. The structure should be demolished. No value for money for Taxpayers	



<b>Project Number</b>	CDF/227	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Shibinga secondary school	
<b>Project Activity</b>	Construction of twin laboratory	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	47%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	B	
<b>Comments</b>	Whereas the project is incomplete, there is a strong feeling that the money allocated could have been enough to support construction of one wing of the laboratory to its completion before commencing work on the second wing. The walls of the incomplete structure are already weathering and may increase the cost as renovations may be necessary to strengthen the building. There is no value for money in the project in its present status.	



<b>Project Number</b>	CDF/011	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Buchifi primary school	
<b>Project Activity</b>	Construction of administration block	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	60%	
<b>Date of Assessment</b>	15/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although construction of the administration block at Buchifi primary school is still ongoing, there are strong indications that the project has been well implemented so far. The bricks are strong and the workmanship is outstanding. The work done is indeed commensurate to the amount spent on the project.	



<b>Project Number</b>	CDF/012	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Buchifi secondary school	
<b>Project Activity</b>	Construction of administration block	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	17/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Just like the work in the primary section, the administration block is so far well implemented with quality standard materials and the workmanship is remarkable. There is value for money in this project and the community expressed their satisfaction with the ongoing work.	



<b>Project Number</b>	CD/014	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Bedas Bukaya primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	53%	
<b>Date of Assessment</b>	15/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project is ongoing, it is well built so far and reflects value for money. It is vital that the project be concluded to minimize damages to the walls due to exposure to weather as this can culminate into more costs. The materials used are of good quality and the workmanship is remarkable.	



<b>Project Number</b>	CDF/015	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Bedas Bukaya Secondary	
<b>Project Activity</b>	Construction of 2 staff houses	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	53%	
<b>Date of Assessment</b>	15/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	According to the project status report, the project activity was the construction of 4 classrooms and not 2 staff houses as indicated in the summary table. Generally, the project is well implemented so far but the continuous exposure to weather is already showing its toll as the brick walls are already showing signs of weathering.	



<b>Project Number</b>	CDF/017	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bumini primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	403,357	
<b>Total Funds Spent to Date</b>	403,357	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	07/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project is incomplete, it is well implemented as evidenced with the quality of materials used and the workmanship so far. Besides, the project cost appears underestimated. The project promises to offer value for money upon completion.	


<b>Project Number</b>	CDF/018	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Teresa's Bumini secondary school	
<b>Project Activity</b>	Constr. of 3 new classrooms.	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,550,000	
<b>Total Funds Spent to Date</b>	1,550,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	53%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The quality of work and materials used in the project is good but the continued exposure of the structure to the vagaries of weather could lead to destruction as evidenced by the falling off of mortar from some of the columns. It passes for a well implemented so far.	


<b>Project Number</b>	CDF/019	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bumwende primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,600,000	
<b>Total Funds Spent to Date</b>	1,600,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	03/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented and fitted with steel windows although it is not yet complete. Generally though, it is well implemented and reflects value for the amount in question.	



<b>Project Number</b>	CDF/022	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Shianda divisional hospital	
<b>Project Activity</b>	Construction of a health facility	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,000,000	
<b>Total Funds Spent to Date</b>	1,000,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented with durable iron sheets, treated wood rafters and good quality bricks. It promises to provide good value for money when completed.	



<b>Project Number</b>	CDF/023	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebubaka primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo/Lureko	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	900,000	
<b>Total Funds Spent to Date</b>	900,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The classes although incomplete, are well built using quality materials and the workmanship is outstanding. The project promises to offer good value for money for the community upon completion.	


<b>Project Number</b>	CDF/024	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebubere primary school	
<b>Project Activity</b>	Construction of classes and administration block	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,880,000	
<b>Total Funds Spent to Date</b>	1,880,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	77%	
<b>Date of Assessment</b>	13/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The physical structure is strong with reinforced column on veranda, quality bricks and colored rough cast finish. Work reflects good value for money so far.	


<b>Project Number</b>	CDF/028	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ekambara primary	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	Nabongo/Lureko	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,700,000	
<b>Total Funds Spent to Date</b>	1,700,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Good quality materials have been used in the project. These include treated timber rafters, durable iron sheets, steel glazed windows and doors. Overall, there is value for taxpayers' money although the project is ongoing.	



<b>Project Number</b>	CDF/032	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emakhwale primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,000,000	
<b>Total Funds Spent to Date</b>	1,000,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	53%	
<b>Date of Assessment</b>	06/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The funds disbursed to the project are below the actual project cost. This partly explains its incomplete status. The project is generally well implemented with good quality treated wood rafters and steel columns although the iron sheets used in roofing are of poor quality. There is value for money in the project so far.	



<b>Project Number</b>	CDF/033		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Maungu primary		
<b>Project Activity</b>	Constr. of 5 new classrooms, roofing, plastering and painting.		
<b>Location/Ward</b>	Etenje		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	1,400,000		
<b>Total Funds Spent to Date</b>	1,400,000		
<b>Total Unaccounted Funds</b>	0		
<b>Technical Performance Score</b>	63%		
<b>Date of Assessment</b>	14/01/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The project is still ongoing and so far there are indications that the funds allocated to the project have been used well. The materials are of standard quality and the workmanship is very remarkable. There is great satisfaction with the project amongst community members. It reflects value for taxpayers' money.		



<b>Project Number</b>	CDF/036	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emukhuwa girls' secondary	
<b>Project Activity</b>	Starting construction of 4 classrooms	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	18/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented as evident in the quality of materials used and the workmanship. There is need however to quicken implementation to limit exposure of the structure to the vagaries of weather.	



<b>Project Number</b>	CDF/038	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Nyapora primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	73%	
<b>Date of Assessment</b>	09/01/00	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the structure has not been painted and glass panes not fitted, the quality of work done so far is impressive and indeed reflects value for taxpayers' money	



<b>Project Number</b>	CDF/039	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Epanja primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	So far, the project is well implemented although some finishing work is still ongoing. It is hoped that the project will run to its conclusion.	



<b>Project Number</b>	CDF/041	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshianderema primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	16/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The school received allocations in 06/07 and 07/08 Financial Years. The work is still ongoing though at a snail pace and so far, there is value for public money.	



<b>Project Number</b>	CDF/044B	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshikalame secondary school	
<b>Project Activity</b>	Construction of laboratory	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	13/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The work done using the sum of money allocated is satisfactory so far. The roofing is not complete yet though the window grills have been fitted and the inside plastered.	



<b>Project Number</b>	CDF/053	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Kamashia primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	400,000	
<b>Total Funds Spent to Date</b>	400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	60%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project has been well implemented so far and seems to represent value for taxpayers' money.	



<b>Project Number</b>	CDF/054	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Stephen Kamashia secondary school	
<b>Project Activity</b>	Construction of twin laboratory	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,150,000	
<b>Total Funds Spent to Date</b>	2,150,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The materials used in the construction of the facility are of good quality and the workmanship so far is good. Although the project is ongoing, it reflects value for taxpayers' money.	



<b>Project Number</b>	CDF/055	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Khabakaya primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing and in Use	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	17/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented so far as evidenced by the workmanship and quality of materials used in its construction. The project is already serving the purpose for which it was intended to serve but should be taken to conclusion to serve the community optimally.	



<b>Project Number</b>	CDF/057	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Khaimba Secondary.	
<b>Project Activity</b>	Construction of twin laboratory	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented so far and should be taken to conclusion in good time to limit exposure of the structure to the vagaries of weather.	



<b>Project Number</b>	CDF/058		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Khaunga secondary school		
<b>Project Activity</b>	Construction of twin laboratory and 4 classrooms		
<b>Location/Ward</b>	East Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	2,450,000		
<b>Total Funds Spent to Date</b>	2,450,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	53%		
<b>Date of Assessment</b>	15/01/09		
<b>Project Classification</b>	C		
<b>Comments</b>	Quality bricks have been used in implementation of the project. The workmanship is indeed impressive and value for taxpayers' money is evident in the project.		



<b>Project Number</b>	CDF/060		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Lukongo primary school		
<b>Project Activity</b>	Construction of 4 classes		
<b>Location/Ward</b>	South Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing and in Use		
<b>Total Funds Awarded to Date</b>	1,400,000		
<b>Total Funds Spent to Date</b>	1,400,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	70%		
<b>Date of Assessment</b>	23/02/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The project is well implemented with treated wood rafters, steel windows and doors. Overall, it reflects value for money.		



<b>Project Number</b>	CDF/062	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Lureko primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo /Matawa	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing and in Use	
<b>Total Funds Awarded to Date</b>	1,358,638	
<b>Total Funds Spent to Date</b>	1,358,638	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	67%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented with good treated wood rafters and fitted grills and a strong concreted floor with screed.	



<b>Project Number</b>	CDF/064	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mabanga primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,450,000	
<b>Total Funds Spent to Date</b>	1,450,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	23/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although two classes have been roofed, two are yet to be done. The structures are well constructed and the steel glass glazed windows well fixed. The doors are also well done.	

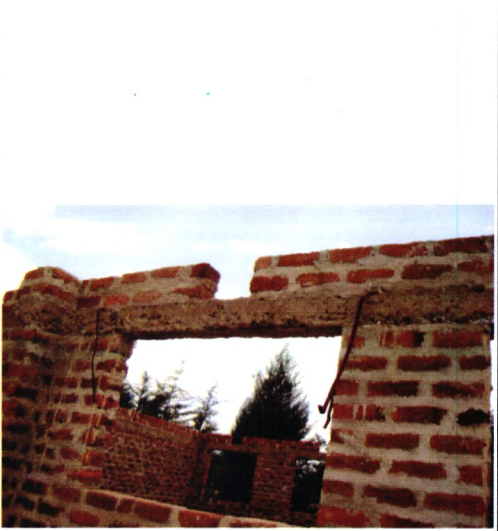
<b>Project Number</b>	CDF/065	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mahola primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	700,000	
<b>Total Funds Spent to Date</b>	700,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	59%	
<b>Date of Assessment</b>	16/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the amount allocated is small to fully implement the project, it is commendable that 50% of the work is already done and represents value for taxpayers' money.	



<b>Project Number</b>	CDF/242	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Patrick Lusheya primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Musanda	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	700,000	
<b>Total Funds Spent to Date</b>	700,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although generally well implemented, the amount allocated is inadequate to facilitate its completion. There is significant level of community satisfaction with the project and it promises to provide value for money upon successful completion.	



<b>Project Number</b>	CDF/067	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Malaha primary school	
<b>Project Activity</b>	Construction of 9 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,300,000	
<b>Total Funds Spent to Date</b>	2,300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	73%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is generally well implemented going by the quality of the physical structure. It provides value for taxpayers' money. So far, it is a well implemented project.	



<b>Project Number</b>	CDF/068	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Maraba secondary school	
<b>Project Activity</b>	Construction of twin laboratory	
<b>Location/Ward</b>	E. Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	19/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented and within the project cost although it is incomplete as the fascia board and other finishing operations has not been conducted. All in all, it reflects value for taxpayers' money.	


<b>Project Number</b>	CDF/071	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	ACK Milimani Girls' High school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	03/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is so far well implemented with two classrooms fully completed. There is value for taxpayers' money.	



<b>Project Number</b>	CDF/076	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Township primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,100,000	
<b>Total Funds Spent to Date</b>	1,100,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	60%	
<b>Date of Assessment</b>	13/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project is ongoing it is well built so far given the quality of materials used and the quality of workmanship.	



<b>Project Number</b>	CDF/079		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	St. Matthew Mung'anga secondary		
<b>Project Activity</b>	Construction of a twin laboratory		
<b>Location/Ward</b>	East Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	1,500,941		
<b>Total Funds Spent to Date</b>	1,500,941		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	53%		
<b>Date of Assessment</b>	16/02/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The work undertaken so far on the physical structure is of good quality although there is the feeling that the cost should be half of the amount spent on the project. Overall though, the project is of good quality.		



<b>Project Number</b>	CDF/081		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Musanda primary school		
<b>Project Activity</b>	Construction of 4 classes		
<b>Location/Ward</b>	South Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	1,400,000		
<b>Total Funds Spent to Date</b>	1,400,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	73%		
<b>Date of Assessment</b>	14/01/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The project is well implemented with quality roofing iron sheets and treated wood rafters and a smooth plaster finish. Painting is yet to be done though.		


<b>Project Number</b>	CDF/082		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Musanda secondary school		
<b>Project Activity</b>	Completion of library /HoD office		
<b>Location/Ward</b>	South Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	300,000		
<b>Total Funds Spent to Date</b>	300,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	73%		
<b>Date of Assessment</b>	16/01/09		
<b>Project Classification</b>	C		
<b>Comments</b>	Although the project is well implemented, the ceiling is not yet fixed. The project has been fitted with both quality doors and windows, hence it is well implemented. The project promises to offer good value for money upon completion.		



<b>Project Number</b>	CDF/085	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Muslim girls secondary school	
<b>Project Activity</b>	Construction of Admin block and roofing of 4 classes	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	13/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project has been well implemented, it is not fully done as the ceiling is yet to be fixed. So far, it represents value for taxpayers' money.	



<b>Project Number</b>	CDF/086	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Muslim primary school	
<b>Project Activity</b>	Construction of 4 classes, water pump and latrines	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,100,000	
<b>Total Funds Spent to Date</b>	2,100,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	09/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project is ongoing, it is satisfactorily implemented so far and looks like there is value for taxpayers' money.	



<b>Project Number</b>	CDF/089	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mwitoti secondary school	
<b>Project Activity</b>	Construction of two storey building	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,200,000	
<b>Total Funds Spent to Date</b>	2,200,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	77%	
<b>Date of Assessment</b>	06/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project is ongoing, it is well done and there is undoubtedly value for taxpayers' money in the project.	


<b>Project Number</b>	CDF/090	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Nyapeta ACK primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete but in use	
<b>Total Funds Awarded to Date</b>	1,650,000	
<b>Total Funds Spent to Date</b>	1,650,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented and already serving the purpose for which it was intended. It will be more useful to the school upon full completion. There is value for money in the project.	



<b>Project Number</b>	CDF/095	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Mary girls secondary school	
<b>Project Activity</b>	Construction of storage and tuition block	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete but in use	
<b>Total Funds Awarded to Date</b>	1,000,000	
<b>Total Funds Spent to Date</b>	1,000,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	73%	
<b>Date of Assessment</b>	09/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Whereas the project is incomplete, all indications point out that it is a well implemented project. The workmanship is impressive and the materials are of standard quality. The project promises to offer value for money to the community upon its successful completion.	



<b>Project Number</b>	CDF/096		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	St. Paul Ebusia secondary school		
<b>Project Activity</b>	Construction of twin laboratory		
<b>Location/Ward</b>	East Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Incomplete and not in use		
<b>Total Funds Awarded to Date</b>	1,500,000		
<b>Total Funds Spent to Date</b>	1,500,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	70%		
<b>Date of Assessment</b>	12/01/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The project is well built so far going by the quality of workmanship and materials used: treated wood rafters, steel doors and windows and, good quality bricks.		



<b>Project Number</b>	CDF/097		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	St. Peter's Mumias High School		
<b>Project Activity</b>	Construction of tuition block ,laboratory and classes		
<b>Location/Ward</b>	Central Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	500,000		
<b>Total Funds Spent to Date</b>	500,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	70%		
<b>Date of Assessment</b>	09/01/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The work undertaken so far on the project depicts quality and value for taxpayers' money. The columns are strong and reinforced with Y16 bars and the bricks are of good quality.		



<b>Project Number</b>	CDF/090	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Nyapeta ACK primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete but in use	
<b>Total Funds Awarded to Date</b>	1,650,000	
<b>Total Funds Spent to Date</b>	1,650,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented and already serving the purpose for which it was intended. It will be more useful to the school upon full completion. There is value for money in the project.	



<b>Project Number</b>	CDF/095	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Mary girls secondary school	
<b>Project Activity</b>	Construction of storage and tuition block	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete but in use	
<b>Total Funds Awarded to Date</b>	1,000,000	
<b>Total Funds Spent to Date</b>	1,000,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	73%	
<b>Date of Assessment</b>	09/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Whereas the project is incomplete, all indications point out that it is a well implemented project. The workmanship is impressive and the materials are of standard quality. The project promises to offer value for money to the community upon its successful completion.	


<b>Project Number</b>	CDF/096	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Paul Ebusia secondary school	
<b>Project Activity</b>	Construction of twin laboratory	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete and not in use	
<b>Total Funds Awarded to Date</b>	1,500,000	
<b>Total Funds Spent to Date</b>	1,500,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well built so far going by the quality of workmanship and materials used: treated wood rafters, steel doors and windows and, good quality bricks.	



<b>Project Number</b>	CDF/097	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Peter's Mumias High School	
<b>Project Activity</b>	Construction of tuition block ,laboratory and classes	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	500,000	
<b>Total Funds Spent to Date</b>	500,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	09/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The work undertaken so far on the project depicts quality and value for taxpayers' money. The columns are strong and reinforced with Y16 bars and the bricks are of good quality.	



<b>Project Number</b>	CDF/098	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ugana primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,000,000	
<b>Total Funds Spent to Date</b>	1,000,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	10/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the final finishing has not been done on the facility, it is well built and represents value for money. It has been fitted with good quality windows and doors, the plastering is well done and so is the roofing. Good value for taxpayers' money.	



<b>Project Number</b>	CDF/099	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Wang'nyang primary school	
<b>Project Activity</b>	Construction of 8 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete but in use	
<b>Total Funds Awarded to Date</b>	2,800,000	
<b>Total Funds Spent to Date</b>	2,800,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	73%	
<b>Date of Assessment</b>	24/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	There is no doubt that the project is well implemented although incomplete. The facility is already in use and is expected to serve the school optimally once completed.	



<b>Project Number</b>	CDF/141	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eluche dispensary	
<b>Project Activity</b>	Construction of a dispensary	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	500,000	
<b>Total Funds Spent to Date</b>	500,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	19/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented and fitted with quality doors and windows. The roofing is also good although it's not painted.	



<b>Project Number</b>	CDF/152	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Enyapora dispensary	
<b>Project Activity</b>	Construction of a dispensary	
<b>Location/Ward</b>	Isongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	2,069,769	
<b>Total Funds Spent to Date</b>	2,069,769	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	08/01/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Work on the health facility is ongoing and there are strong indications that the project is well implemented. Quality materials have been used and it has been fitted with fine steel glass glazed windows and doors. The shelves and wardrobes were being fixed at the time of NTA visit. The project promises to provide value for taxpayers' money upon completion.	



<b>Project Number</b>	CDF/237	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Maungu primary school	
<b>Project Activity</b>	Construction of 5 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	60%	
<b>Date of Assessment</b>	24/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The construction is of good quality as demonstrated by the quality of materials used and the workmanship. The project reflects value for taxpayers' money.	


<b>Project Number</b>	CDF/239	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bumini Technical Training Institute	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	500,000	
<b>Total Funds Spent to Date</b>	500,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	07/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project is generally well implemented, the amount allocated is inadequate to facilitate its completion. The workmanship is so far good but could be better.	


<b>Project Number</b>	CDF/013	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Buchitu primary	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	700,000	
<b>Total Funds Spent to Date</b>	700,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	17/02/09	
<b>Project Classification</b>	D	
<b>Comments</b>	Despite the fact that the project is incomplete, it has not received money in the succeeding financial years. In its present state, it amounts to utter wastage of taxpayers' money.	



<b>Project Number</b>	CDF/021	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Butobe primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	The quality of work done is good and the materials used are of standard size. However, there has been a delay in completion of the project. The delay is partly attributed to the limited and irregular funding to the project.	



<b>Project Number</b>	CDF/034		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Emuberi primary		
<b>Project Activity</b>	Starting construction of 4 classes		
<b>Location/Ward</b>	South Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Incomplete		
<b>Total Funds Awarded to Date</b>	300,000		
<b>Total Funds Spent to Date</b>	300,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	50%		
<b>Date of Assessment</b>	15/01/09		
<b>Project Classification</b>	D		
<b>Comments</b>	Whereas it is obvious that the above allocated amount is grossly insufficient to undertake the project activity, the project has not received additional funding. The fact that the walls are already weathering illustrates that it has been in this state for a long time and may result into additional costs.		



<b>Project Number</b>	CDF/037		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Emukhuwa primary		
<b>Project Activity</b>	Construction of 4 classes		
<b>Location/Ward</b>	South Wanga		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Incomplete		
<b>Total Funds Awarded to Date</b>	400,000		
<b>Total Funds Spent to Date</b>	400,000		
<b>Total Unaccounted Funds</b>	Nil		
<b>Technical Performance Score</b>	60%		
<b>Date of Assessment</b>	20/02/09		
<b>Project Classification</b>	D		
<b>Comments</b>	Just as in the above case, the financial allocation to this project has been inadequate to complete the project. In spite of the inadequacy, the project has not received additional funding and amounts to wastage of public money in its present state as it is not serving community needs.		


<b>Project Number</b>	CDF/052	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Iyabo primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	The project has been well implemented as demonstrated by the good quality of materials used and good workmanship. The work done is satisfactory so far going by the amount allocated to it. However, it amounts to a waste of taxpayers' money as it is not serving the community. There is need to allocate more funds to the project to enable its completion.	


<b>Project Number</b>	CDF/056	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Khabondi primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	15/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	The weathering that is evident on the wall is an indication that the project has been in this state for a considerably long time. Although the work done is impressive, there is need to allocate adequate funds to facilitate completion of the project otherwise it remains a waste of taxpayers' money in its present state.	


<b>Project Number</b>	CDF/059	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Lubinu primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	56%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	Whereas the project is incomplete, it did not receive financial allocation in the succeeding financial years as provided by the CDF Act. It is not serving the community at present and there is need to allocate it more funding.	



<b>Project Number</b>	CDF/072	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Milimani DEB primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	03/02/09	
<b>Project Classification</b>	D	
<b>Comments</b>	Although the project is incomplete, it did not receive financial allocation in the succeeding financial years as provided by the CDF Act. It is not serving the community at present and there is need to allocate it more funding.	



<b>Project Number</b>	CDF/080	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Muroni primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	12/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	It is important that the project be allocated adequate funding to facilitate its completion. The weathering on the walls will likely culminate into increased costs in project implementation.	

<b>Project Number</b>	CDF/083	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Musango primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	23/02/09	
<b>Project Classification</b>	D	
<b>Comments</b>	The project did not receive financial allocation in the subsequent financial year to facilitate its completion. It is not serving the community in the present state and at best amounts to wastage of taxpayers' money.	

<b>Project Number</b>	CDF/088	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mwichina primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	19/02/09	
<b>Project Classification</b>	D	
<b>Comments</b>	The project did not receive financial allocation in the subsequent financial year to facilitate its completion. It is not serving the community in the present state and at best amounts to wastage of taxpayers' money.	


<b>Project Number</b>	CDF/092	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Shibale primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	14/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	The project did not receive financial allocation in the subsequent financial year to facilitate its completion. It is not serving the community in the present state and at best amounts to wastage of taxpayers' money.	


<b>Project Number</b>	CDF/094	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Shitoto primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	400,000	
<b>Total Funds Spent to Date</b>	400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	60%	
<b>Date of Assessment</b>	13/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	The project did not receive financial allocation in the subsequent financial year to facilitate its completion. It is not serving the community in the present state and at best amounts to wastage of taxpayers' money.	



<b>Project Number</b>	149	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Malaha health centre	
<b>Project Activity</b>	Construction of a health facility.	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Incomplete	
<b>Total Funds Awarded to Date</b>	200,000	
<b>Total Funds Spent to Date</b>	200,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	20%	
<b>Date of Assessment</b>	15/01/09	
<b>Project Classification</b>	D	
<b>Comments</b>	Whereas the allocation is insufficient to undertake the project activity, the project did not receive financial allocation in the subsequent financial year. There is need to avail adequate funding to the project for the community to realize optimal value for money.	



## Annex 2



Project Classification Summary Tables,  
Project Profiles and digital photographs  
for all CDF projects visited and assessed in  
the Financial Year (FY) 2007 - 08



<b>Project Number</b>	CDF/008	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Butende Secondary	
<b>Project Activity</b>	Construction of administration block	
<b>Location/Ward</b>	Musanda	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	2,210,000	
<b>Total Funds Spent to Date</b>	2,210,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	90%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was well implemented and has good finishing as seen in the above photo. The roof was well done and fitted with a neat fascia board. There is indeed value for money in the project.	



<b>Project Number</b>	CDF/009	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Buyundo primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Musanda	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,500,000	
<b>Total Funds Spent to Date</b>	1,500,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	90%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	Generally, the project is well implemented as demonstrated in the finishing work. The painting is impeccable and the external wall has been given a good roughcast finish. The fittings especially the windows and doors are well fitted and the veranda satisfactorily supported. It is a well implemented project.	



<b>Project Number</b>	CDF/012	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebubole primary	
<b>Project Activity</b>	Construction of four classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete and in use	
<b>Total Funds Awarded to Date</b>	1,100,000	
<b>Total Funds Spent to Date</b>	1,100,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	87%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The classes are well done to MoE specifications and the workmanship is very remarkable. It is complete and in use and the community expressed satisfaction with the facility. It is a well implemented project.	



<b>Project Number</b>	CDF/014	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ekambara primary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,700,000	
<b>Total Funds Spent to Date</b>	1,700,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The materials used in the construction of the classes are of standard quality and the workmanship is laudable. The roof is well done and fitted with a neatly done fascia board. The finishing work is very commendable.	



<b>Project Number</b>	CDF/015	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eluche Secondary school	
<b>Project Activity</b>	Construction of administration block	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,500,000	
<b>Total Funds Spent to Date</b>	1,500,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	93%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The administration block is spacious, stable and well designed. The finishing work is almost impeccable as indicated by the well done rough cast and the strong pillars. The doors and windows are well fitted and in a nutshell, the project indeed represents value for money.	


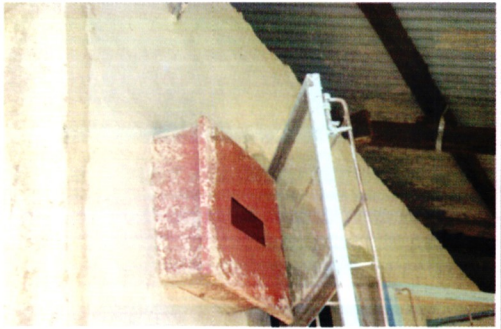
<b>Project Number</b>	CDF/017	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emachina primary school	
<b>Project Activity</b>	Construction of Administration block	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete and in Use	
<b>Total Funds Awarded to Date</b>	1,410,000	
<b>Total Funds Spent to Date</b>	1,410,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	This is a well done project and reflects value for money. The painting is well done and overall workmanship is meticulous. The school administration expressed satisfaction with the work done in the school.	



<b>Project Number</b>	CDF/021	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Enyapora primary	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project has seriously enhanced the learning environment in the school. It was identified by the community following a serious shortage of learning space. The classrooms are constructed in accordance with MOE specifications and the community expressed satisfaction with the project. It is well implemented.	



<b>Project Number</b>	CDF/027	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Indangalasia Secondary school	
<b>Project Activity</b>	Construction of 4 classroom	
<b>Location/Ward</b>	Shibinga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,050,000	
<b>Total Funds Spent to Date</b>	1,050,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	98%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project reflects good value for money. The physical structure is up to standard and the finishing is good. There is great satisfaction with the project. Good value for money.	


<b>Project Number</b>	CDF/028	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ingusi primary school	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	2,000,000	
<b>Total Funds Spent to Date</b>	2,000,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	97%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The amount of work done is indeed indicative of the project costs. The materials used are of standard quality and the workmanship quite impressive as evidenced in the fine painting and general finishing. There is value for money in the project.	


<b>Project Number</b>	CDF/037	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mabanga primary school	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	Isongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	1,450,000	
<b>Total Funds Spent to Date</b>	1,450,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	93%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was identified by the School Management Committee. The community played a role in its implementation not only by donating labour but also construction materials especially timber and sand. The fittings – doors and windows are of standard quality and well fitted.	

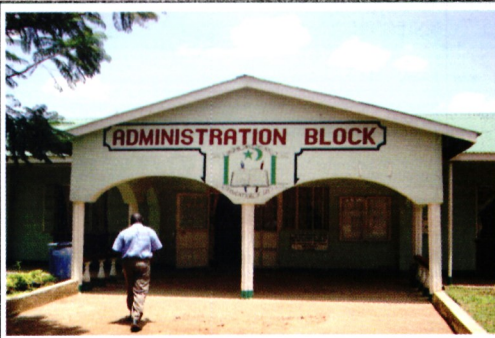
<b>Project Number</b>	CDF/038B	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Malaha primary school	
<b>Project Activity</b>	Installation of Power.	
<b>Location/Ward</b>	Malaha	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	121,000	
<b>Total Funds Spent to Date</b>	121,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The School Management Committee proposed the project which has been done well; the wiring was professionally done and the school is currently having electricity. The school administration and the community in general expressed great satisfaction with the project.	



<b>Project Number</b>	CDF/039	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Maraba Secondary School	
<b>Project Activity</b>	Construction of a Twin Laboratory.	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	86%	
<b>Date of Assessment</b>	11/009/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The amount of work done at the institution is commensurate to the amount of money in question. The materials are of standard quality more so, the iron sheets. The laboratory is fitted with quality steel glass glazed windows and doors. The workmanship is good and the finishing very professionally done. There is value for money in the project.	



<b>Project Number</b>	CDF/040A	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Matawa Secondary school	
<b>Project Activity</b>	Construction of Administration block	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,700,000	
<b>Total Funds Spent to Date</b>	1,700,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	93%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The administration block is complete and in use. Quality materials have been used in the construction work and the workmanship is remarkable as evidenced in the fine finishing especially, the painting and flooring. There is certainly value for money in the project.	


<b>Project Number</b>	CDF/040B	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Matawa Secondary school	
<b>Project Activity</b>	Power supply	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	126,000	
<b>Total Funds Spent to Date</b>	126,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The money was paid directly to Kenya Power and Lighting Company which in turn installed electricity in the school. The power has greatly improved the learning environment in the institution and the community as well as the school administrators expressed overall satisfaction with the project. It indeed represents value for taxpayers' money.	


<b>Project Number</b>	CDF/046.	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mungabira primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,900,000	
<b>Total Funds Spent to Date</b>	1,900,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	05/02/09	
<b>Project Classification</b>	A	
<b>Comments</b>	Although the project cost seems to be on the upper side, the project has been well implemented and the finishing is good. It reflects value for money.	



<b>Project Number</b>	CDF/049	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Muslim Girls' Secondary	
<b>Project Activity</b>	Construction of Administration block	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	96%	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was well implemented as demonstrated by the quality of materials used and the highly remarkable workmanship. The work done is indeed commensurate to the amount of money spent on the project.	



<b>Project Number</b>	CDF/050	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Muslim Primary School	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	2,100,000	
<b>Total Funds Spent to Date</b>	2,100,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	86%	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	A	
<b>Comments</b>	The classes are constructed according to MoE standards and have greatly improved the learning environment in the school. The project is complete and in use thus serving the intended purpose. There is value for money in the project.	

<b>Project Number</b>	CDF/054.	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Petro's primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	90%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is complete and well implemented. The finishing and fittings are of good quality and there is a manifestation of good workmanship. The classes are fitted with steel doors and windows and the verandah is strongly supported by pillars. There is value for taxpayers' money in the project.	



<b>Project Number</b>	CDF/076.	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshikulu Community Health Centre	
<b>Project Activity</b>	Const. of a Health Centre	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	2,500,000	
<b>Total Funds Spent to Date</b>	2,500,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	A	
<b>Comments</b>	The project that was started by a self group in the community to respond to the needs of the community members is complete and well implemented. The CDF support was a great boost to the project. The finishing's and fittings are well done and electricity is installed in the facility. It reflects good value for money.	


<b>Project Number</b>	CDF/078.	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mung'ang'a Dispensary	
<b>Project Activity</b>	Construction of a Health facility	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	1,928,515	
<b>Total Funds Spent to Date</b>	1,928,515	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	14/09/09.	
<b>Project Classification</b>	A	
<b>Comments</b>	The dispensary has been constructed using bricks reinforced with back column. Treated wood rafters have been used in roofing. Generally, the project is well implemented and reflects value for taxpayers' money.	


<b>Project Number</b>	CDF/079	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Enyapora Dispensary	
<b>Project Activity</b>	Construction of a Dispensary	
<b>Location/Ward</b>	Isongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	2,069,769	
<b>Total Funds Spent to Date</b>	2,069,769	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	90%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	Quality materials have been used and it has been fitted with fine steel glass glazed windows and doors. The shelves and wardrobes are well fitted. The project offers value for taxpayers' money.	



<b>Project Number</b>	CDF/086	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Buriya water project	
<b>Project Activity</b>	Sinking of a borehole	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	70,000	
<b>Total Funds Spent to Date</b>	70,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is well implemented with a concrete base. The pump is in a good condition and is well protected with a barbed wire fence. It serves the community needs and there is overall satisfaction with the work undertaken.	



<b>Project Number</b>	CDF/087.	<b>Picture Unavailable</b>
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebuyenjere primary	
<b>Project Activity</b>	Borehole and pump	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	100,000	
<b>Total Funds Spent to Date</b>	100,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The installed water pump is working well and the community did confirm that indeed the facility is meeting their identified need at its inception. There project reflects value for taxpayers' money.	



<b>Project Number</b>	CDF/090	 
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emukhalari water project	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	50,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The spring is well protected and the community is now confident that indeed they have access to only clean but also safe water from the spring. The community identified the project and strongly participated in its implementation. There is value for money in the project.	


<b>Project Number</b>	CDF/093	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emukhalari water project	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	50,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The spring is well protected and the community is now confident that indeed they have access to only clean but also safe water from the spring although it require routine maintenance to remove sand and stones. The community identified the project and strongly participated in its implementation. There is value for money in the project.	


<b>Project Number</b>	CDF/096	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ichinga water and Sanitation	
<b>Project Activity</b>	Spring protection.	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	50,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was identified by the community at a chief baraza. Community members provided sand and also contributed labour during the implementation process. The spring is well protected and has a fine plaster to the sides. There is overall community satisfaction with the project.	


<b>Project Number</b>	CDF/097	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ichingo water project	
<b>Project Activity</b>	Installation of a pump	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	70,000	
<b>Total Funds Spent to Date</b>	70,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The work done is commensurate to the amount of money spent on the project. It is serving community needs and there is overall satisfaction with the project. It reflects value for taxpayers' money.	



<b>Project Number</b>	CDF/0103	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Lureko /Matawa water project	
<b>Project Activity</b>	Pump installation.	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	50,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A.	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	A	
<b>Comments</b>	The community identified the project and provided labor and sand during the implementation process. The pump is of great quality and serving the community efficiently. The work done on the facility represents value for money spent on the project.	


<b>Project Number</b>	CDF/105	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mashebwebwe water project	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	50,000	
<b>Technical Performance Score</b>	N/A	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was identified by the community at a chief baraza. Community members provided sand and also contributed labour during the implementation process. The spring is well protected and has a fine plaster to the sides. There is overall community satisfaction with the project.	



<b>Project Number</b>	CDF/108	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mayala water project	
<b>Project Activity</b>	Sinking a borehole and pump installation	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	70,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	70,000	
<b>Technical Performance Score</b>	N/A	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The work done is commensurate to the amount of money spent on the project. It is serving community needs and there is overall satisfaction with the project. It reflects value for taxpayers' money.	



<b>Project Number</b>	CDF/110	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Musanda Community water	
<b>Project Activity</b>	Piping water	
<b>Location/Ward</b>	Musanda	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	440,000	
<b>Total Funds Spent to Date</b>	440,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The community fully participated in the project through the Project Management Committee. The piping is well done and water is available to community members at selected points. The community members did confirm that the project indeed meets their needs.	


<b>Project Number</b>	CDF/111	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Musango water project	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	70,000	
<b>Total Funds Spent to Date</b>	70,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was selected by the community and the CDF largely supported the labour costs and material purchase. The project is well implemented and represents value for money.	



<b>Project Number</b>	CDF/114	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mwitawa	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>		
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	50,000	
<b>Technical Performance Score</b>	N/A	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project is a community initiative. Community members largely donated materials while the CDF kitty supported labour costs and purchase of cement for use in the project. It is complete and serving the needs of community members. Certainly, there is value for taxpayers' money.	



<b>Project Number</b>	CDF/115	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ndalusia	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	50,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	N/A	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	Community members largely donated materials while the CDF kitty supported labour costs and purchase of cement for use in the project. It is complete and serving the needs of community members. There is value for taxpayers' money in this project.	



<b>Project Number</b>	CDF/118	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Shibale Environmental	
<b>Project Activity</b>	Borehole ,pump and security wall	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	200,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	200,000	
<b>Technical Performance Score</b>	N/A	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	A	
<b>Comments</b>	The project was identified by the community members and they also played a leading role in its implementation. The water pump is well protected inside a strong security wall and community members pay Kshs 2 for a container of 20 litres. There is overwhelming community satisfaction with the project and indeed it represents value for money.	



<b>Project Number</b>	CDF/002	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ahonginjo Sec. School.	
<b>Project Activity</b>	Construction of three classes	
<b>Location/Ward</b>	Musanda	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	40%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	There was a strong feeling that the amount of money already spent on the project is much higher compared to the work done. The amount in question it was noted should have been adequate to complete the project. In its present state, the windows and doors are not fitted and the internal and external finishing is not yet done.	



<b>Project Number</b>	CDF/004	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bukaya primary	
<b>Project Activity</b>	Construction of one class	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	40%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	Poor workmanship is evident in the project especially in walling. It also appears that the bricks used in the construction are of substandard quality as demonstrated by the cracks in some areas. The project is so far poorly implemented.	



<b>Project Number</b>	CDF/013	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebuyenjere primary	
<b>Project Activity</b>	Construction of 4 classrooms & Purchase of 3 acres of Land.	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The school acquired the piece of land and constructed four semi-permanent classrooms. Although the decision to put up the semi-permanent structures was informed by the amounts allocated to the project, it was not a wise decision especially in the long term. There is no value for money in the project.	



<b>Project Number</b>	CDF/025	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ichinga primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,100,000	
<b>Total Funds Spent to Date</b>	1,100,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	49%.	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	There is a strong feeling that the amount of work done in the school is not commensurate to the amount spent so far on the project. Despite the significant financial allocation, the project has taken unnecessarily long to complete and the workmanship is suspect as demonstrated by the leaning pillars in the above photo.	



<b>Project Number</b>	CD/029	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Isango primary school	
<b>Project Activity</b>	Construction of 5 classrooms	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,100,000	
<b>Total Funds Spent to Date</b>	1,100,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The school seriously needs the classes that were undergoing construction as at the time of NTA visit. However, it was observed that the classes have been constructed using poor quality bricks and the verandah has been poorly supported as demonstrated by the bending pillars. The project does not reflect value for money.	



<b>Project Number</b>	CDF/035	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Lureko Girls' sec school	
<b>Project Activity</b>	Construction of 4 Classrooms.	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	1,800,000	
<b>Total Funds Spent to Date</b>	1,800,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	Whereas Ksh 1.8M has been allocated to the project, work on the classes is barely half way complete. The classes are not serving the needs of the school in their present state and the workmanship is also questionable. The project does not reflect value for money spent so far.	

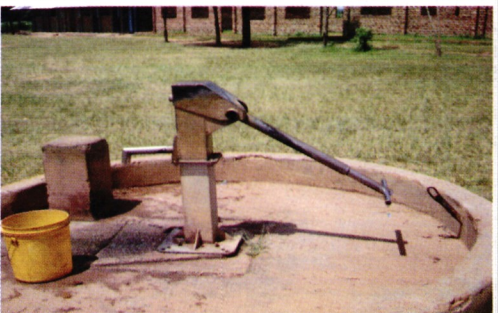

<b>Project Number</b>	CDF/038A	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Malaha primary school	
<b>Project Activity</b>	Construction of 4 c/rooms.	
<b>Location/Ward</b>	Malaha	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	2,300,000	
<b>Total Funds Spent to Date</b>	2,300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	49%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	Compared to other schools in the constituency, Malaha has received significant sum of money for the construction of the same number of classes if not even less. However, the project does not reflect value for money as poor quality materials have been used in construction for instance, the substandard steel used in the fittings. Poor workmanship is also evident in walling and painting. There is hardly value for money in the project.	



<b>Project Number</b>	CDF/079	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Iwasi Drift	
<b>Project Activity</b>	Construction of a bridge	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	2,000,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	2,000,000	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The project was overwhelmingly selected by the community members as it is important in enhancing accessibility especially during the rainy season. Despite its importance, the project was poorly implemented as the drainage keeps blocking during the rains diverting water into farms often with disastrous consequences. It is also widely felt that the amount of work done is not commensurate to the amount of money in question.	



<b>Project Number</b>	CDF/082	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshitukhumi Drift	
<b>Project Activity</b>	Construction of a bridge	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	2,000,000	
<b>Total Funds Spent to Date</b>	2,000,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	B.	
<b>Comments</b>	The project was identified by the community members during a chief's baraza. It is critical to the community especially in rainy season. The workmanship is poor especially on the guard rails and the plastering work has been done poorly. There is an extreme mismatch between the work done and the amount of money in question.	


<b>Project Number</b>	CDF/084	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mabanga Drift	
<b>Project Activity</b>	Construction of a bridge	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	2,000,000	
<b>Total Funds Spent to Date</b>	2,000,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	40%.	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	Despite the colossal sum of money allocated and spent on the project, it is poorly done and it is only a matter of time before the bridge collapses. It is a poorly implemented project and does not reflect value for money.	


<b>Project Number</b>	CDF/089	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebwaliro Water project	
<b>Project Activity</b>	Construction of a pump	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	50,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The project was identified by the community members at a chief's baraza. The community provided materials (hard core) and labour. However, the borehole was shallowly done and the community cannot get water from the facility. The CDF amount was used to acquire the pump. In the present state, there is totally no value for money in this project.	



<b>Project Number</b>	CDF/095	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emukhuwa primary school	
<b>Project Activity</b>	Installation of water pump	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	70,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	70,000	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The project was initially undertaken by Kenfico but the pump developed a problem. The CDF allocation was used to replace the pump and as at the time of NTA visit, the pump was working and serving the needs of community members. There is however the strong feeling that the amount of money spent is higher than the work undertaken thus, lack of value for taxpayers' money.	


<b>Project Number</b>	CDF/099	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ikoli water project	
<b>Project Activity</b>	Protection of spring	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	50,000	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The project was initiated by the community and each member of the Community contributed Kshs.20, sand and stones towards the protection of the spring. CDF funds were used to purchase cement and to pay for labour. However, the spring produces small volume of water that cannot meet the needs of the community members. The value for money in the project is indeed questionable.	



<b>Project Number</b>	CDF/0100	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Kamashia Water project	
<b>Project Activity</b>	Sinking a borehole and pump installation	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	150,000	
<b>Total Funds Spent to Date</b>	150,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	Although the community selected the project, it was badly implemented. It is not serving the intended purpose in spite of the fact that the allocated amount should have been adequate to complete the work. NTA realized that the Project Management Committee mistook the amount as a gift from the area MP and used it for their personal benefit. This is a waste of taxpayers' money and all the concerned parties should account for their involvement in this fraud.	



<b>Project Number</b>	CDF/106	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Matawa water project	
<b>Project Activity</b>	Drilling of a borehole.	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	50,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The community identified the project and contributed materials especially sand and labour. However, the project is poorly implemented as the borehole is not fitted with a pump making the water susceptible to contamination. There is hardly value for money in the project.	



<b>Project Number</b>	CDF/113	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mwibwi	
<b>Project Activity</b>	Spring protection	
<b>Location/Ward</b>	East.	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Complete.	
<b>Total Funds Awarded to Date</b>	50,000	
<b>Total Funds Spent to Date</b>	0	
<b>Total Unaccounted Funds</b>	50,000	
<b>Technical Performance Score</b>	48%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	B	
<b>Comments</b>	The community not only identified the project but also contributed materials (sand, labour and stones). Although the project was well implemented, measures were not taken to ensure sanitation and hygiene around the facility. The water point was very dirty and posed a serious health risk to community members as at the time of NTA visit.	



<b>Project Number</b>	CDF/003		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Buchifi Primary		
<b>Project Activity</b>	Construction of Administration block		
<b>Location/Ward</b>	Etenje		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	300,000		
<b>Total Funds Spent to Date</b>	300,000		
<b>Total Unaccounted Funds</b>	0		
<b>Technical Performance Score</b>	60%		
<b>Date of Assessment</b>	11/09/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The quality of the physical structure is good with reinforced VRC beam. The amount is however inadequate to finish the project. It is hoped the project will receive additional funding in the next financial year.		



<b>Project Number</b>	CDF/005	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bukaya secondary	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	This is a well implemented project. The project cost responds to the amount of work already undertaken on the facility and the workmanship is remarkable. So far, there is value for money in the project.	



<b>Project Number</b>	CDF/006	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bumini primary	
<b>Project Activity</b>	Construction of 4 Classrooms	
<b>Location/Ward</b>	East Wang'a	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	403,357	
<b>Total Funds Spent to Date</b>	403,357	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The amount of work done so far is immense bearing in mind the total allocation to the project as at the time of field visit. The materials used are of standard quality and the workmanship exhibits great professionalism on the side of the contractor. There is need to avail adequate funds to the project to enhance its completion.	



<b>Project Number</b>	CDF/007	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bumwende primary	
<b>Project Activity</b>	Construction of 4 Classrooms	
<b>Location/Ward</b>	Shibinga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,600,000	
<b>Total Funds Spent to Date</b>	1,600,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Quality materials have been used in the project as evident in the steel windows and doors fitted. The plastering work has been well done although work was ongoing as at the time of NTA visit. There is overall community satisfaction with the project and there is certainly value for money in this facility. So far, it is a well implemented project.	



<b>Project Number</b>	CDF/010	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebubaka primary	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	900,000	
<b>Total Funds Spent to Date</b>	900,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	This is a well implemented project and the amount of work done indeed reflect the amount of money spent so far. Good workmanship is evident especially on walling and roofing. The windows and doors are yet to be fitted. The school administration and members of the community expressed satisfaction with the project that promises to seriously improve the learning conditions in the school.	



<b>Project Number</b>	CDF/011	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ebubere primary	
<b>Project Activity</b>	Construction of a Admin. block and Classrooms	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,880,000	
<b>Total Funds Spent to Date</b>	1,880,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	87%.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The classrooms were constructed in line with MoE specifications and are well done with standard quality materials and the workmanship is very impressive. The administration block is yet to be completed but there are strong signs that it is well implemented so far as reflected in the quality of workmanship and the materials used. The project reflects value for money and there is widespread satisfaction with the projects at the community level.	



<b>Project Number</b>	CDF/016	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Elwasambi Primary school	
<b>Project Activity</b>	Construction of two Class-rooms	
<b>Location/Ward</b>	Shibinga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	400,000	
<b>Total Funds Spent to Date</b>	400,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	60%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the classrooms are incomplete as painting work and fittings are not yet done, there are indications that the project has been well implemented as reflected in the quality of materials used and the quality of workmanship that is highly remarkable. The veranda has been supported with strong pillars and there is certainly value for taxpayers' money in the project.	


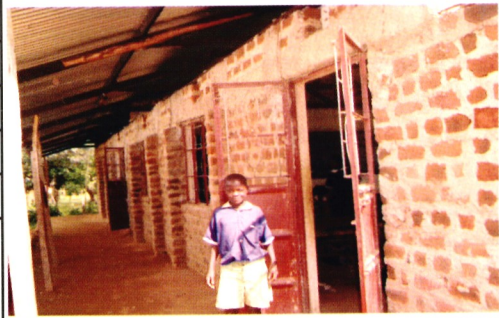
<b>Project Number</b>	CDF/018	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emakhwale Primary school	
<b>Project Activity</b>	Construction of four Class-rooms	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,000,000	
<b>Total Funds Spent to Date</b>	1,000,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Although the project has been well implemented, there is a strong feeling that the amount in question should have been sufficient to complete the project. The materials used in the project are of good especially the bricks and roofing materials. The school administration and the community in general expressed satisfaction with the implementation of the project.	


<b>Project Number</b>	CDF/019	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emaungu primary school	
<b>Project Activity</b>	Construction of 5 classes	
<b>Location/Ward</b>	Etenje	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	57%.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The funds allocated to the project have been limited to facilitate its successful completion. There is need to avail more funds to the project to enable its completion so that the school can realize its optimal value. The project is so far well done and the school administration expressed their satisfaction with the project.	



<b>Project Number</b>	CDF/020	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emukhuwa Secondary school	
<b>Project Activity</b>	Construction of 4 Classrooms	
<b>Location/Ward</b>	Etenje	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	67%.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The amount in question is very limited to support construction of four classrooms. There is need to avail adequate funds to the project in order to facilitate its completion. Good quality treated wood rafters and steel columns have been used in the project and the workmanship is so far remarkable.	



<b>Project Number</b>	CDF/022	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Epanja primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Malaha	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	80%.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is nearly complete with most of the remaining work having to do with finishing. Quality materials have been used in the project for instance steel doors and windows and quality bricks. Both the internal and external plastering work has been well done and the overall workmanship is satisfactory. There is value for money in the project.	



<b>Project Number</b>	CDF/023	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshiakhulo primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	70%.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project was identified by the PTA and the community actively participated in its implementation through contribution of labor. A significant percentage of the work is already undertaken using quality materials and the standard of workmanship is impressive. There is value for taxpayers' money in the project.	



<b>Project Number</b>	CDF/024	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshianderema primary school	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	Lusheya	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	57%.	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The school is in dire need of the classrooms and is waiting with bated breath for their completion. However, the amount allocated to the project is inadequate to support implementation of the projects to completion. There is strong feeling amongst the school administrators and the wider community that the funds have been well spent.	



<b>Project Number</b>	CDF/026	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ihonje secondary school	
<b>Project Activity</b>	Construction of 4 classrooms	
<b>Location/Ward</b>	Etenje	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	85%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	This project was initiated following demolition of the initial classes that were poorly done and failed to meet the MOE specifications. The current classes that are undergoing construction have been expanded in accordance with MOE standards and there is optimism that they will serve the school well upon completion. The school administration noted the need to allocate the school more funds as the student population is drastically increasing yet they have no single class at the moment. Note that the school is still hosted in the primary section.	



<b>Project Number</b>	CDF/030	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Kamashia Secondary	
<b>Project Activity</b>	Construction of twin laboratory	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,150,000	
<b>Total Funds Spent to Date</b>	2,150,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	60%.	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Up to this point the project is well implemented and it reflects value for money. Strong pillars have been used to support the verandah and the structure has been neatly fitted with a fascia board. Besides the wall finishing is great and there is certainly value for money in the project.	



<b>Project Number</b>	CDF/031	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Khabakaya primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	800,000	
<b>Total Funds Spent to Date</b>	800,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	73%.	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is so far well implemented but the funding has been inadequate to complete four classrooms. The project was selected by the school management committee and good work has been undertaken. The materials are of good quality as evidenced by the remarkable workmanship and the materials used. The community expressed satisfaction with the project.	



<b>Project Number</b>	CDF/032		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Khaimba secondary school		
<b>Project Activity</b>	Twin Laboratory and Power supply		
<b>Location/Ward</b>	Isongo		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing.		
<b>Total Funds Awarded to Date</b>	926,000		
<b>Total Funds Spent to Date</b>	926,000		
<b>Total Unaccounted Funds</b>	0		
<b>Technical Performance Score</b>	70%		
<b>Date of Assessment</b>	11/09/09		
<b>Project Classification</b>	C		
<b>Comments</b>	The project is well implemented so far. Out of the entire project allocation, Kshs.126, 000 was used to install power in the facility and the rest went into construction of the laboratory. Although the laboratory is incomplete, it reflects value for money but there is need for more resources to facilitate its completion so that the school can realize full value for money. So far, it is a well implemented project.		



<b>Project Number</b>	CDF/033		
<b>Constituency</b>	Mumias		
<b>Project Name</b>	Khaunga secondary school		
<b>Project Activity</b>	Construction of twin laboratory		
<b>Location/Ward</b>	Malaha		
<b>MPs Name</b>	Hon. Benjamin Washiali		
<b>Project Status</b>	Ongoing		
<b>Total Funds Awarded to Date</b>	2,450,000		
<b>Total Funds Spent to Date</b>	2,450,000		
<b>Total Unaccounted Funds</b>	0		
<b>Technical Performance Score</b>	80%		
<b>Date of Assessment</b>	11/09/09		
<b>Project Classification</b>	C		
<b>Comments</b>	This is a well implemented project. The bricks used are of standard quality and the roofing and walling are well done. One wing is already fitted with quality steel doors and windows and painted. So far, there is value for money in the project although there were isolated cases of stakeholders who felt that the amount should have been adequate to complete the two wings.		



<b>Project Number</b>	CDF/034	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Lukongo primary school	
<b>Project Activity</b>	Construction of 4 Classrooms.	
<b>Location/Ward</b>	Etenje	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	1,400,000	
<b>Total Funds Spent to Date</b>	1,400,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	67%	
<b>Date of Assessment</b>		
<b>Project Classification</b>	C	
<b>Comments</b>	A huge percentage of the work is already done although glasses have not been fitted on the window panes and the painting work was still pending as at the time of visit. Quality materials have been used in implementation of the project and the workmanship is quite impressive. There is value for money in the project.	



<b>Project Number</b>	CDF/036	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Lureko primary school	
<b>Project Activity</b>	Construction of classes	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,358,000	
<b>Total Funds Spent to Date</b>	1,358,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	90%.	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The classes have been constructed in accordance with MoE specifications. Treated wood rafters, steel windows and doors have been used and the classes have a fine painting in the interior. A well done roughcast gives the project a decent external finish and the verandah is strongly supported using pillars. The project reflects value for money and there is overall community satisfaction with the project.	



<b>Project Number</b>	CDF/041	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	ACK Milimani Girls' High school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,300,000	
<b>Total Funds Spent to Date</b>	1,300,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	57%	
<b>Date of Assessment</b>	03/02/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is so far well implemented with two classrooms fully completed and with a raised foundation. Steel doors and windows have been fitted and the walls given a good finish. There is value for taxpayers' money.	



<b>Project Number</b>	CDF/047	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Matthew Mung'ang'a Secondary	
<b>Project Activity</b>	Construction of a twin laboratory	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,500,941	
<b>Total Funds Spent to Date</b>	1,500,941	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	53%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The work undertaken so far on the physical structure is of good quality. The materials too are of good quality and the workmanship indeed reflects value for money. The community and school administration expressed happiness with the project.	


<b>Project Number</b>	CDF/051	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mutono primary school	
<b>Project Activity</b>	Construction of 5 C/Rooms & Administration block	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,000,000	
<b>Total Funds Spent to Date</b>	2,000,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	83%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	As at the time of NTA visit, work on the administration block was still ongoing and had been well done. The materials used were of good quality and the workmanship was impressive. The classes were generally well done and fitted with quality steel doors and windows. The finishing was also great and the workmanship, very commendable. There is definitely value for money in the project.	



<b>Project Number</b>	CDF/052	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Mwitoti secondary school	
<b>Project Activity</b>	Construction of class storey	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,000,000	
<b>Total Funds Spent to Date</b>	2,000,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	79%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	This is a well implemented project. The first floor of the storey building is in use and fitted with steel doors and windows. Strong pillars have been used to support the verandah and there is definitely value for money in the project. The school administration expressed their satisfaction with the project so far.	



<b>Project Number</b>	CDF/053	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Nyapeta	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Etenje	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,650,000	
<b>Total Funds Spent to Date</b>	1,650,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	53%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	So far the project is well implemented although it is still ongoing. The classrooms are fitted with steel doors and windows and strong pillars have been used to support the Verandah. The classes are well done and promises to seriously improve the learning environment in the school.	


<b>Project Number</b>	CDF/055	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Mary girls' Mumias	
<b>Project Activity</b>	Construction of Classrooms-Storey	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	1,000,000	
<b>Total Funds Spent to Date</b>	1,000,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	80%	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	C	
<b>Comments</b>	The project was proposed by the school management committee. So far the project is well implemented although incomplete. It is partly in use and is expected to be of great service to the school once completed. Good value for money to the community.	


<b>Project Number</b>	CDF/056	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Paul's Ebusia Secondary	
<b>Project Activity</b>	Construction of a Twin Laboratory.	
<b>Location/Ward</b>	Malaha	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	1,500,000	
<b>Total Funds Spent to Date</b>	1,500,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	63%.	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	C	
<b>Comments</b>	So far, the funds allocated to the project have been well utilized. The windows have been well fitted and the interior given a fine paint finish. The exterior is yet to be given a finish and there is near consensus among community members that the project represents value for money so far. .	



<b>Project Number</b>	CDF/057	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	St. Peters Mumias high	
<b>Project Activity</b>	Construction of a Laboratory.	
<b>Location/Ward</b>	Nabongo	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	1,500,000	
<b>Total Funds Spent to Date</b>	1,500,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	67%	
<b>Date of Assessment</b>	11/09/09.	
<b>Project Classification</b>	C	
<b>Comments</b>	The project was selected through the School Management Committee. It is well implemented bearing in mind the amount spent so far. The project is however taking too long and should be awarded more funding to enable completion so that the school can realize the optimal value for money.	



<b>Project Number</b>	CDF/059	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Wang'nyang primary school	
<b>Project Activity</b>	Construction of 8 classes	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing but in use	
<b>Total Funds Awarded to Date</b>	2,800,000	
<b>Total Funds Spent to Date</b>	2,800,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	73%	
<b>Date of Assessment</b>	11/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	There is no doubt that the project is well implemented although it is still ongoing. The facility is already in use and is expected to serve the school optimally once completed. The completed classrooms are well finished; fitted with painted doors and windows. The verandah is well done and classrooms fitted nicely with fascia.	



<b>Project Number</b>	CDF/069	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Ugana primary school	
<b>Project Activity</b>	Construction of 4 classes	
<b>Location/Ward</b>	Musanda	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	1,800,000	
<b>Total Funds Spent to Date</b>	1,800,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	83%.	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	So far the project is well implemented and the doors and windows have been fitted although the glasses have not been fixed. Even though the internal and external wall finishing's have not been done, there are indications that the project has been well implemented as reflected in the quality of workmanship demonstrated in this project. There is value for taxpayers' money.	



<b>Project Number</b>	CDF/071	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Bukaya health centre	
<b>Project Activity</b>	Construction of Patient wards	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	779,500	
<b>Total Funds Spent to Date</b>	779,500	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	73%.	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	Though the doors and windows are yet to be fixed, the funds allocated to the project seem to have been put into good use. The materials used especially the iron sheets, are of good quality and the foundation is strongly built and adequately raised thus sufficiently protecting the structure from floods. The structure is also supported using strong pillars and there is definitely value for taxpayers' money.	

<b>Project Number</b>	CDF/073.	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eluche dispensary	
<b>Project Activity</b>	Construction of a Dispensary	
<b>Location/Ward</b>	East Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali.	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	500,000	
<b>Total Funds Spent to Date</b>	500,000	
<b>Total Unaccounted Funds</b>	Nil	
<b>Technical Performance Score</b>	70%	
<b>Date of Assessment</b>	12/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project is well implemented and fitted with quality doors and windows. The roofing is also good and fitted with a neatly painted fascia board and ceiling board. Internal fittings though are yet to be done. There is value for money in the project.	

<b>Project Number</b>	CDF/074	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Emuchimi Health centre	
<b>Project Activity</b>	Construction of health centre	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	2,200,000	
<b>Total Funds Spent to Date</b>	2,200,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	50%	
<b>Date of Assessment</b>	14/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The amount of work already undertaken on the facility is commensurate to the amount in question. The project has taken a relatively long time to implement and as such more costs related to inflation have been accommodated. However, it passes for a well implemented project as demonstrated by the good finishing on the internal and external walls, the quality fittings used – steel doors and windows and, the neatly fitted fascia board. The project promises to offer optimal value for money upon completion.	

<b>Project Number</b>	CDF/075	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Eshikalame Health centre	
<b>Project Activity</b>	Constr. of Health Centre.	
<b>Location/Ward</b>	South Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing	
<b>Total Funds Awarded to Date</b>	300,000	
<b>Total Funds Spent to Date</b>	300,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	63%	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	The project was selected by the community who also contributed bricks and labour during its implementation. Although incomplete, the project is so far well implemented and represents value for money. The community expressed their happiness with the project and expressed their anxiety towards its completion.	

<b>Project Number</b>	CDF/077.	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Kamashia Health Centre	
<b>Project Activity</b>	Construction of health centre	
<b>Location/Ward</b>	Central Wanga	
<b>MPs Name</b>	Hon. Benjamin Washiali	
<b>Project Status</b>	Ongoing.	
<b>Total Funds Awarded to Date</b>	500,000	
<b>Total Funds Spent to Date</b>	500,000	
<b>Total Unaccounted Funds</b>	0	
<b>Technical Performance Score</b>	50%.	
<b>Date of Assessment</b>	15/09/09	
<b>Project Classification</b>	C	
<b>Comments</b>	So far, the project is well implemented. Quality materials have been used in the construction of the health centre and the workmanship is indeed outstanding. The community expressed their satisfaction with the project and demanded for its completion. There is value for money in the project.	

<b>Project Number</b>	54	
<b>Constituency</b>	Mumias	
<b>Project Name</b>	Kanorero sec. school	
<b>Project Activity</b>	Renovation	
<b>Location/Ward</b>	Muguru	
<b>MPs Name</b>	Benjamin Washiali	
<b>Project Status</b>	Complete	
<b>Date of Visit</b>	09/03/09	
<b>Total Funds Awarded to Date</b>	750,000	
<b>Total Funds Spent to Date</b>	745,000	
<b>Total Unaccounted Funds</b>	5,000	
<b>Technical Performance Score</b>	67%	
<b>Project Classification</b>	C	
<b>Comments</b>	The school has received a great facelift and has definitely improved the learning environment. The renovation work at the facility has introduced an element of elegance. There is value for money in the project.	

**Annex 3**  
**CDF Project Rapid Assessment Form**

Recommendation (mark one box)	Stage 1 = OK	Stage 2 = Further Investigation	Report No.	

Constituency Name		Location/Ward	
Project Name		Project Number	
Project Activity		Rural/Urban	
MPs Name (2007)		MPs Name (2008)	

Project Status	Complete		Incomplete/stalled		Ongoing		Does not exist	
----------------	----------	--	--------------------	--	---------	--	----------------	--

Amount Awarded	FY 2007/08	FY 2006/07	FY 2006/05	FY 2005/04
Kshs.				

Total CDF Funds Spent to date (April 2009) Kshs.	
--	--

Total Other Funds Spent to date (April 2009) Kshs. (NGOs, CBOs, FBOs, Private Sector, etc.)	
--	--

Total Funds Spent to date (April 2009) Kshs.	
--	--

CDF Project Manager Name		Contact Nos	
Project Contractor Name		Contact Nos	
Other Contact Person		Contact Nos	

**Field Visit Assessment Information**

Name or general position of people met at project site	
1.	3.
2.	4.

Project Score	Out of 10	Comments
Community participation in selection/community/users satisfaction		
Project completion status -- on time/within budget?		
Visual assessment of overall quality of construction and finish		
Total Project Rapid Score (out of 30)		

Note: A mark of 10 is excellent, while a mark of 1 is very bad

Signature of RO:		Time and Date:	
------------------	--	----------------	--

## Annex 4

### CDF Project Users Questionnaire

Quest. No.:
-------------

Name of RO
------------

#### Instructions for RO

- Explain who you are, and the purpose of your visit. Clearly state that the interview is anonymous.
- Ask the person if they know about the concerned project before starting the interview, if they have no knowledge then do not interview them.
- If the person agrees to be interviewed, ask how long they have been resident in the community. If it is less than six months do not undertake the interview. Do not interview people directly or officially involved in managing the project as they will have a bias.
- ROs must interview a mix of women and men at all project locations.
- The minimum requirement is 4 user interviews/project.
- In questions with written answers be very clear and concise.

1. Name of District		2. Constituency Name	
3. Name of Project		4. Location Name	
5. Gender of person interviewed (circle one answer number)		1. Female	2. Male
6. Age of person interviewed		_____ years	
7. Occupation (circle one answer number)	1. Farmer 2. Business Owner 3. Labourer /Housekeeper	4. Private Sector Employee 5. Government employee 6. Other (explain) _____	
8. RO -- Why have you selected this person? (list relationship to project)	1. Resident lives near project 2. Resident from community uses the project 3. Other (explain) _____		
9. Do you know who funded the project?		1. Yes                      2. No	
10. If yes, can you say who?	1. CDF 2. LATF 3. MP	4. Community 5. Donors/NGOs 6. Government	7. Councillor 8. Private company 9. Do not know 10. Other (explain) _____
11. Is the project complete and in use, or incomplete and in use?	1. Project is completed and in use 2. Project is completed and not in use 3. Project is incomplete and in use 4. Project is incomplete and not in use 5. Project is "missing", does not exist		
12. Please explain your answer? (If the person choose option 2, 3, 4, or 5)	_____ _____		
13. Did you or people you know in the community participate in project selection?	1. Yes, community participated 2. No, community did not participate 3. Do not know		
14. If yes, please explain how you know this?	1. I attended the meeting 2. I know people who attended and they told me 3. Other (explain) _____		
15. If yes, do you know approximately how many people attended the meeting to select the project?	1. _____ people (write the number) 2. Do not know		
16. If yes to Q10, (community participated in project selection), Was this project selected as a priority for this community?	1. Yes 2. No 3. Do not know		

17. If no to Q10, do you know who selected the project?	1. MP 2. Councillor	3. Chief/Govt. official 4. Do not know	5. Other _____
18. Did you or people you know in the community participate in project implementation?	1. Yes, community participated 2. No, community did not participate 3. Do not know		
19. If yes, how?	1. They contributed labour/security/supervision/goods/materials/land etc. 2. They gave money 3. Other (explain) _____		
20. Was there a Project Management Committee formed for this project?	1. Yes	2. No	3. Do not know
21. If yes, who selected this Committee?	1. MP selected 2. Community selected 3. MP and community	4. Councillor selected 5. Govt. selected	6. Do not know 7. Other (explain) _____
22. What is your satisfaction in terms of quality of the facility and value for money spent on this project?	1. Very satisfied 2. Satisfied	3. Dissatisfied 4. Very dissatisfied	
23. If Dissatisfied or Very dissatisfied, explain why?			
24. Was this project transparently managed?	1. Yes 2. No	3. Do not know	
25. If no, explain why not?			
26. How would you rate the project in terms of impact on beneficiaries?	1. High impact – many people in community benefited 2. Medium impact – some people in community benefited 3. Low impact – none/few people in community benefited		
27. What are the three most important future projects for this community?	1. _____		
	2. _____		
	3. _____		
28. Can you suggest ways to improve implementation of CDF/LATF projects?	1. _____		
	2. _____		
	3. _____		
29. RO Verification -- What is the actual completion status of the project based on observation? (visit the project and then complete this question)	1. Project is completed and in use		
	2. Project is completed and not in use		
	3. Project is incomplete and in use		
	4. Project is incomplete and not in use		
	5. Project is “missing”, does not exist		

Name of interviewer	Signature of interviewer	Date and time of interview

## Annex 5

### Technical Project Assessment Form

Project Score (Out of 100)	%	Project No.	
Project Type (LATF/CDF)		Project No.	

Project Name		Constituency Name	
--------------	--	-------------------	--

District Name		Location / Ward Name	
---------------	--	----------------------	--

Area	Out of 10	Justify the score you gave with explanation below (write clearly and neatly)
(1) Quality of materials used		
(2) Project completion status -- on time/within budget?		
(3) Project cost – does it represent value for money		
Total (total the marks given out of 30, then list %)		<b>What is your overall recommendation (circle one answer)</b> 1. Project <u>has been</u> well implemented and looks as though there is good value for money for the community. 2. Project <u>has not been well</u> implemented and looks as though funds have not been well used. 3. Is difficult to fully assess.
	%	

**Note: A mark of 10 is excellent, while a mark of 1 is very bad.**

Name of technical reviewer:	Date:
Signature of technical reviewer:	Time:

## Annex 6



March, 10<sup>th</sup> 2010

Hon. Benjamin Washiali,  
Member of Parliament for Mumias Constituency,  
Nairobi

Dear Hon. Washiali,

**RE: MUMIAS CDF CONSTITUENCY CITIZEN REPORT CARD**

The National Taxpayers Association (NTA) is a national, independent and non-partisan organization committed to working in partnership with the government and other stakeholders to promote transparency, effectiveness and accountability in the use of government resources. The NTA is currently compiling and disseminating Citizens' Report Cards on the provision of services and the management of devolved funds in constituencies and local authorities across Kenya. On 16<sup>th</sup> March 2009, the NTA launched 23 Citizen Report Cards on the management of CDF in 23 constituencies in all eight provinces.

Under Phase 2 of the NTAs national CDF monitoring programme an additional 26 constituencies have been selected, one of which is the constituency you represent, **Mumias**. In honor of your esteemed office as the representative of Mumias constituents in Parliament, the NTA herein encloses a draft copy of the Mumias Constituency CDF Citizens' Report Card for your comments.

The NTA, which is committed to objective, evidence-based reporting on CDF performance to the public, seeks a formal partnership with you to improve the implementation of CDF in Ganze constituency. The NTA has the capacity and tools to strengthen CDF Committees in key areas, such as community consultation to identify priority projects and procurement to ensure value for money in the construction of projects, among others.

The NTA is committed to working with you to improve the performance of CDF in your constituency. Should you be interested in such a partnership then the NTA is willing to clearly explain this in the attached Mumias Constituency Citizens' Report Card prior to printing and dissemination. Please call Mr. Nashon Odhiambo on 0734 500 940 at the NTA Secretariat office to arrange a meeting to discuss this further.

The NTA is a national, volunteer-based, independent and non-partisan organization established to improve the delivery of services and the management of devolved funds for the benefit of all Kenyans.

NTA is a citizen initiative currently steered by the following National Governing Council members: Kenya Private Sector Alliance (KEPSA) - Chair, National Informal Sector Coalition (NISCO) - Vice Chair, Institute of Certified Public Accountants of Kenya (ICPAK) - Treasurer, Centre for Governance and Development (CGD) - Secretary, Kenya Female Advisory Organization (KEFEADO) - Deputy Secretary, Supreme Council of Kenya Muslims (SUPKEM) - Member, Kenya Private Sector Network (KPSA Network) - Member, African Woman and Child Feature Service (AWCFS) - Member, United Business Association (UBA) - Member, Catholic Justice & Peace Commission (CJPC), Kenya Alliance of Resident Associations (KARA) and Transparency International Kenya (TI-K) - Member.  
National Taxpayers Association, P.O. Box 4037-00506, Nairobi, Kenya. Tel: 020-3861813/4. Website: www.nta.or.ke

Kindly note that lack of feedback by 19<sup>th</sup> March, 2010 on the draft CRC will be considered as a confirmation of the report and we will proceed with printing and dissemination through a formal launch.

We look forward to hearing from you soon.

Yours Faithfully,



Kennedy Masime,  
**National Secretary, NTA &  
Executive Director, Centre for Governance and Development (CGD)**

C.C. Ms. Agnes Odhiambo  
Chief Executive Officer  
CDF Coordination Board  
Harambee Co-operative Plaza  
10<sup>th</sup> Floor  
Nairobi

## Annex 7



18<sup>th</sup> March 2010

Hon. Benjamin Washiali,  
MP, Mumias Constituency,  
Nairobi.

Dear Hon. Washiali,

**RE: Thank you**

On behalf of the National Taxpayers Association, I write to thank you for your support and commitment to improved management/performance and impact of the CDF in your constituency.

We appreciate the active involvement of your office during the data collection phase in Mumias constituency and the strong affirmation by your Personal Assistant through a telephone discussion on 16<sup>th</sup> March 2010 that indeed the report was a true reflection of facts with regard to CDF projects in the constituency. We also acknowledge your interest in working with us on practical solutions to respond to the findings of our submitted draft Citizen's Report Card (CRC) for Mumias constituency.

As discussed with the PA, we are looking forward to a meeting with you to discuss the proposed partnership that we referred to in our first letter to your office. We hope that you find an opportune moment for this important meeting.

We remain open to clarifying any section of this letter that may not be clear.

Yours Faithfully,

Kennedy Masime,  
**Executive Director, Centre for Governance and Development (CGD) &  
National Secretary, NTA**

The NTA is a national, volunteer-based, independent and non-partisan organization established to improve the delivery of services and the management of devolved funds for the benefit of all Kenyans.

NTA is a citizen initiative currently steered by the following National Governing Council members: Kenya Private Sector Alliance (KEPSA) - Chair, National Informal Sector Coalition (NISCO) - Vice Chair, Institute of Certified Public Accountants of Kenya (ICPAK) - Treasurer, Centre for Governance and Development (CGD) - Secretary, Kenya Female Advisory Organization (KEFEADO) - Deputy Secretary, Supreme Council of Kenya Muslims (SUPKEM) - Member, Kenya Private Sector Network (KPSA Network) - Member, African Woman and Child Feature Service (AWCFS) - Member, United Business Association (UBA) - Member, Catholic Justice & Peace Commission (CJPC), Kenya Alliance of Resident Associations (KARA) and Transparency International Kenya (TI-K) - Member.  
National Taxpayers Association, P.O. Box 4037-00506, Nairobi, Kenya. Tel: 020-3861813/4. Website: www.nta.or.ke

## **Annex 8**

### List of MP's that met with NTA or sent comments on the draft CDF CRC

<b>No.</b>	<b>Name of MP</b>	<b>Constituency</b>	<b>Date of sending 1st Letter</b>	<b>Date of sending reminder</b>	<b>Date of meeting</b>
1	Hon. Samuel Kazungu	Kaloleni	31st August 09	19th October 09	18th November 09
2	Hon. Oburu Odinga	Bondo	31st August 09	19th October 09	2nd November 09
3	Hon. N. Warugongo	Kieni	31st August 09	19th October 09	19th November 09
4	Hon. Simon Mbugua	Kamukunji	31st August 09	-	9th September 09
5	Hon. Nicholas Gumbo	Rarieda	21st October 09	-	19th September 09
6	Hon. Ababu Namwamba	Budalangi	20th November 09	-	3rd December 09
7	Hon. David Were	Matungu	19th January 2010	-	4th February 2010
8	Hon. S. Ojaamongson	Amagoro	19th January 2010	-	16th February 2010
9	Hon. Benjamin Washiali	Mumias	4th March 2010	-	16th March 2010



National Taxpayers Association  
**pesa zetu, haki yetu**

#### **HEAD OFFICE**

**National Taxpayers Association (NTA)**  
Riara Gardens, off Riara Road  
Adjacent to Makini Schools  
P. O. Box 4037 - 00506, City Stadium, Nairobi, Kenya  
Telephone: 254-20-3861813/4  
Cell Phone: 254-734-500940  
Email: [admin@nta.or.ke](mailto:admin@nta.or.ke)  
Website: [www.nta.or.ke](http://www.nta.or.ke)

**Nairobi Regional Office**  
Riara Gardens, off Riara Road  
Adjacent to Makini Schools  
P.O. Box 27527 - 00506  
Telephone: 254-20-3861821  
Nairobi West  
Cell Phone: 254-738-992660  
Email: [nairobi@nta.or.ke](mailto:nairobi@nta.or.ke)

**Eastern Regional Office**  
Town Plaza, 3rd Floor, Ngei Road  
P.O. Box 2046 90100  
Machakos  
Cell Phone: 254-738-992666  
Email: [eastern@nta.or.ke](mailto:eastern@nta.or.ke)

**Western Regional Office**  
at Legio, along Hotel Generation Way  
Adjacent to Three Storey Residential  
Opposite International Child Support (I.C.S)  
P.O. Box 474-50400  
Busia  
Cell Phone: 254-738-992667  
Email: [western@nta.or.ke](mailto:western@nta.or.ke)

**Rift Valley Regional Office**  
Meadows Hse, 1st Floor, Room 106  
Opposite Sirikwa Hotel  
P.O. Box 4956-30100  
Eldoret  
Cell Phone: 254-738-992663  
Email: [rftvalley@nta.or.ke](mailto:rftvalley@nta.or.ke)

**Central Regional Office**  
Nyeri Teachers Plaza, 1st Floor, Room 10  
P.O. Box 576 - 10100  
Nyeri  
Cell Phone: 254-738-992661  
Email: [central@nta.or.ke](mailto:central@nta.or.ke)

**Coast Regional Office**  
Kanderbhoy Building  
Nkurumah Road, 1st Floor, Suite 14, Opp Co-Op Bank  
P.O. Box 98860  
Mombasa  
Cell Phone: 254-738-992664  
Email: [coast@nta.or.ke](mailto:coast@nta.or.ke)

**Nyanza Regional Office**  
Mosata Plaza, Ground Floor  
Oginga Odinga Road  
P.O. Box 204-40123  
Kisumu  
Cell Phone: 254-738-992668  
Email: [nyanza@nta.or.ke](mailto:nyanza@nta.or.ke)

**North Eastern Regional Office**  
Jihan Centre, 1st Floor, Room 7  
Harambee Road  
P.O. Box 1235-70100  
Garissa  
Cell Phone: 254-738-992665  
Email: [northeastern@nta.or.ke](mailto:northeastern@nta.or.ke)

